

CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS

ID	Task Name	Duration	Start	Finish	2012				2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
1																																																												
2	1 - KATELLA AVENUE	2780 days	Mon 4/1/13	Sun 11/26/23	1 - KATELLA AVENUE																																																							
3	1A - LEWIS TO E/O STATE COLLEGE	322 days	Tue 10/1/13	Thu 12/25/14	LEWIS TO E/O STATE COLLEGE																																																							
4	Bid / Award / NTP	3 emo	Tue 10/1/13	Mon 12/30/13	Bid / Award / NTP																																																							
5	Construction	12 emo	Mon 12/30/13	Thu 12/25/14	Construction																																																							
6	1B - E/O STATE COLLEGE TO HOWELL	900 days	Fri 7/1/16	Fri 12/13/19	1B - E/O STATE COLLEGE TO HOWELL																																																							
7	Administration	3 emo	Fri 7/1/16	Thu 9/29/16	Administration																																																							
8	Preliminary Engineering	3 emo	Thu 9/29/16	Wed 12/28/16	Preliminary Engineering																																																							
9	Final PS&E	12 emo	Wed 12/28/16	Sat 12/23/17	Final PS&E																																																							
10	FHWA Review & Approval (Hwy of National Significance)	18 emo	Fri 7/1/16	Sat 12/23/17	FHWA Review & Approval (Hwy of National Significance)																																																							
11	Right of Way Acquisition	12 emo	Sun 9/24/17	Wed 9/19/18	Right of Way Acquisition																																																							
12	Bid / Award / NTP	3 emo	Wed 9/19/18	Tue 12/18/18	Bid / Award / NTP																																																							
13	Construction	12 emo	Tue 12/18/18	Fri 12/13/19	Construction																																																							
14	1C - SR-57 TO SANTA ANA RIVER	643 days	Wed 7/1/20	Sun 12/18/22	1C - SR-57 TO SANTA ANA RIVER																																																							
15	Administration	3 emo	Wed 7/1/20	Tue 9/29/20	Administration																																																							
16	Preliminary Engineering	3 emo	Tue 9/29/20	Mon 12/28/20	Preliminary Engineering																																																							
17	Final PS&E	9 emo	Mon 12/28/20	Fri 9/24/21	Final PS&E																																																							
18	Right of Way Acquisition	12 emo	Mon 12/28/20	Thu 12/23/21	Right of Way Acquisition																																																							
19	Bid / Award / NTP	3 emo	Thu 12/23/21	Wed 3/23/22	Bid / Award / NTP																																																							
20	Construction	9 emo	Wed 3/23/22	Sun 12/18/22	Construction																																																							
21	1D - ANAHEIM BOULEVARD TO MANCHESTER	756 days	Fri 1/1/21	Sun 11/26/23	1D - ANAHEIM BOULEVARD TO MANCHESTER																																																							
22	Administration	3 emo	Fri 1/1/21	Thu 4/1/21	Administration																																																							
23	Preliminary Engineering	3 emo	Thu 4/1/21	Wed 6/30/21	Preliminary Engineering																																																							
24	Final PS&E	12 emo	Wed 6/30/21	Sat 6/25/22	Final PS&E																																																							
25	Right of Way Acquisition	12 emo	Mon 12/6/21	Thu 12/1/22	Right of Way Acquisition																																																							
26	Bid / Award / NTP	3 emo	Thu 12/1/22	Wed 3/1/23	Bid / Award / NTP																																																							
27	Construction	9 emo	Wed 3/1/23	Sun 11/26/23	Construction																																																							

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months

Administration		Right of Way Acquisition		Construction		Milestone	
Preliminary Engineering		Final PS&E		Task		Summary	
Right of Way Engineering		Bid / Award / NTP		Split		Progress	



CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS

ID	Task Name	Duration	Start	Finish	2012				2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
28	1E - MANCHESTER TO ANAHEIM WAY	258 days	Mon 4/1/13	Thu 3/27/14	ER TO ANAHEIM WAY																																																							
29	Bid / Award / NTP	3 emo	Mon 4/1/13	Sun 6/30/13	Bid / Award / NTP																																																							
30	Construction	9 emo	Sun 6/30/13	Thu 3/27/14	Construction																																																							
31	1F - ANAHEIM WAY TO LEWIS	841 days	Fri 7/1/16	Sat 9/21/19	1F - ANAHEIM WAY TO LEWIS																																																							
32	Administration	3 emo	Fri 7/1/16	Thu 9/29/16	Administration																																																							
33	Preliminary Engineering	3 emo	Thu 9/29/16	Wed 12/28/16	Preliminary Engineering																																																							
34	Final PS&E	12 emo	Wed 12/28/16	Sat 12/23/17	Final PS&E																																																							
35	Right of Way Acquisition	12 emo	Mon 7/3/17	Thu 6/28/18	Right of Way Acquisition																																																							
36	Bid / Award / NTP	3 emo	Thu 6/28/18	Wed 9/26/18	Bid / Award / NTP																																																							
37	Construction	12 emo	Wed 9/26/18	Sat 9/21/19	Construction																																																							
38	2 - STATE COLLEGE BOULEVARD	1818 days	Sat 1/2/16	Wed 12/21/22	2 - STATE COLLEGE BOULEVARD																																																							
39	2A - ORANGEWOOD TO S/O KATELLA	777 days	Sat 1/2/16	Wed 12/26/18	2A - ORANGEWOOD TO S/O KATELLA																																																							
40	Administration	3 emo	Sat 1/2/16	Fri 4/1/16	Administration																																																							
41	Preliminary Engineering	3 emo	Fri 4/1/16	Thu 6/30/16	Preliminary Engineering																																																							
42	Final PS&E	12 emo	Thu 6/30/16	Sun 6/25/17	Final PS&E																																																							
43	Right of Way Acquisition	9 emo	Thu 1/5/17	Mon 10/2/17	Right of Way Acquisition																																																							
44	Bid / Award / NTP	3 emo	Mon 10/2/17	Sun 12/31/17	Bid / Award / NTP																																																							
45	Construction	12 emo	Sun 12/31/17	Wed 12/26/18	Construction																																																							
46	2B - KATELLA TO N/O HOWELL (grade sep.)	1558 days	Sun 1/1/17	Wed 12/21/22	2B - KATELLA TO N/O HOWELL (grade sep.)																																																							
47	Administration	6 emo	Sun 1/1/17	Fri 6/30/17	Administration																																																							
48	Final PS&E	18 emo	Fri 6/30/17	Sat 12/22/18	Final PS&E																																																							
49	RR Agreements / PUC Approval	18 emo	Fri 6/30/17	Sat 12/22/18	RR Agreements / PUC Approval																																																							
50	Right of Way Acquisition	18 emo	Sat 7/7/18	Sun 12/29/19	Right of Way Acquisition																																																							
51	Bid / Award / NTP	6 emo	Mon 1/6/20	Sat 7/4/20	Bid / Award / NTP																																																							
52	Construction	30 emo	Sat 7/4/20	Wed 12/21/22	Construction																																																							

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months

Administration		Right of Way Acquisition		Construction		Milestone	
Preliminary Engineering		Final PS&E		Task		Summary	
Right of Way Engineering		Bid / Award / NTP		Split		Progress	



CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS

ID	Task Name	Duration	Start	Finish	2012				2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
53	2C - S/O ORANGEWOOD TO ORANGEWOOD	386 days	Mon 1/2/17	Tue 6/26/18	2C - S/O ORANGEWOOD TO ORANGEWOOD																																																							
54	Administration	3 emo	Mon 1/2/17	Sun 4/2/17	Administration																																																							
55	Preliminary Engineering	3 emo	Sun 4/2/17	Sat 7/1/17	Preliminary Engineering																																																							
56	Final PS&E	3 emo	Sat 7/1/17	Fri 9/29/17	Final PS&E																																																							
57	Bid / Award / NTP	3 emo	Fri 9/29/17	Thu 12/28/17	Bid / Award / NTP																																																							
58	Construction	6 emo	Thu 12/28/17	Tue 6/26/18	Construction																																																							
59	2D - N/O HOWELL TO N/O CERRITOS	643 days	Wed 7/1/20	Sun 12/18/22	2D - N/O HOWELL TO N/O CERRITOS																																																							
60	Administration	3 emo	Wed 7/1/20	Tue 9/29/20	Administration																																																							
61	Preliminary Engineering	3 emo	Tue 9/29/20	Mon 12/28/20	Preliminary Engineering																																																							
62	Right of Way Acquisition	12 emo	Mon 12/28/20	Thu 12/23/21	Right of Way Acquisition																																																							
63	Final PS&E	12 emo	Mon 12/28/20	Thu 12/23/21	Final PS&E																																																							
64	Bid / Award / NTP	3 emo	Thu 12/23/21	Wed 3/23/22	Bid / Award / NTP																																																							
65	Construction	9 emo	Wed 3/23/22	Sun 12/18/22	Construction																																																							
66	3 - ORANGEWOOD AVENUE	2357 days	Fri 4/1/16	Tue 4/15/25	3 - ORANGEWOOD AVENUE																																																							
67	3A - ANAHEIM WAY TO STATE COLLEGE	706 days	Fri 4/1/16	Mon 12/17/18	3A - ANAHEIM WAY TO STATE COLLEGE																																																							
68	Administration	3 emo	Fri 4/1/16	Thu 6/30/16	Administration																																																							
69	Preliminary Engineering	3 emo	Thu 6/30/16	Wed 9/28/16	Preliminary Engineering																																																							
70	Right of Way Acquisition	12 emo	Wed 9/28/16	Sat 9/23/17	Right of Way Acquisition																																																							
71	Final PS&E	12 emo	Wed 9/28/16	Sat 9/23/17	Final PS&E																																																							
72	Bid / Award / NTP	3 emo	Sat 9/23/17	Fri 12/22/17	Bid / Award / NTP																																																							
73	Construction	12 emo	Fri 12/22/17	Mon 12/17/18	Construction																																																							
74	3B - STATE COLLEGE TO S. DUPONT	708 days	Wed 1/1/20	Sat 9/17/22	3B - STATE COLLEGE TO S. DUPONT																																																							
75	Administration	3 emo	Wed 1/1/20	Tue 3/31/20	Administration																																																							
76	Preliminary Engineering	3 emo	Tue 3/31/20	Mon 6/29/20	Preliminary Engineering																																																							
77	Right of Way Acquisition	12 emo	Mon 6/29/20	Thu 6/24/21	Right of Way Acquisition																																																							
78	Final PS&E	12 emo	Mon 6/29/20	Thu 6/24/21	Final PS&E																																																							
79	Bid / Award / NTP	3 emo	Thu 6/24/21	Wed 9/22/21	Bid / Award / NTP																																																							
80	Construction	12 emo	Wed 9/22/21	Sat 9/17/22	Construction																																																							

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months

Administration		Right of Way Acquisition		Construction		Milestone	
Preliminary Engineering		Final PS&E		Task		Summary	
Right of Way Engineering		Bid / Award / NTP		Split		Progress	



CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS


ID	Task Name	Duration	Start	Finish	2012				2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
81	3C - S. DUPONT TO SANTA ANA RIVER	858 days	Wed 1/1/20	Sat 4/15/23	3C - S. DUPONT TO SANTA ANA RIVER																																																							
82	Administration	3 emo	Wed 1/1/20	Tue 3/31/20	Administration																																																							
83	Preliminary Engineering	3 emo	Tue 3/31/20	Mon 6/29/20	Preliminary Engineering																																																							
84	Final PS&E	12 emo	Mon 6/29/20	Thu 6/24/21	Final PS&E																																																							
85	Right of Way Acquisition	12 emo	Sat 12/26/20	Tue 12/21/21	Right of Way Acquisition																																																							
86	Bid / Award / NTP	4 emo	Tue 12/21/21	Wed 4/20/22	Bid / Award / NTP																																																							
87	Construction	12 emo	Wed 4/20/22	Sat 4/15/23	Construction																																																							
88	3D - SANTA ANA RIVER TO E/O SR-57	856 days	Sat 1/1/22	Tue 4/15/25	3D - SANTA ANA RIVER TO E/O SR-57																																																							
89	Administration	3 emo	Sat 1/1/22	Fri 4/1/22	Administration																																																							
90	Preliminary Engineering	3 emo	Fri 4/1/22	Thu 6/30/22	Preliminary Engineering																																																							
91	Final PS&E	12 emo	Thu 6/30/22	Sun 6/25/23	Final PS&E																																																							
92	Bid / Award / NTP	4 emo	Sun 6/25/23	Mon 10/23/23	Bid / Award / NTP																																																							
93	Construction	18 emo	Mon 10/23/23	Tue 4/15/25	Construction																																																							
94	4 - GENE AUTRY WAY	707 days	Sun 9/1/19	Wed 5/18/22	4 - GENE AUTRY WAY																																																							
95	4A - I-5 TO STATE COLLEGE	707 days	Sun 9/1/19	Wed 5/18/22	4A - I-5 TO STATE COLLEGE																																																							
96	Administration	3 emo	Sun 9/1/19	Sat 11/30/19	Administration																																																							
97	Preliminary Engineering	3 emo	Sat 11/30/19	Fri 2/28/20	Preliminary Engineering																																																							
98	Final PS&E	12 emo	Fri 2/28/20	Mon 2/22/21	Final PS&E																																																							
99	Right of Way Acquisition	12 emo	Fri 2/28/20	Mon 2/22/21	Right of Way Acquisition																																																							
100	Bid / Award / NTP	3 emo	Mon 2/22/21	Sun 5/23/21	Bid / Award / NTP																																																							
101	Construction	12 emo	Sun 5/23/21	Wed 5/18/22	Construction																																																							
102	5 - ANAHEIM WAY	579 days	Tue 10/1/19	Sun 12/19/21	5 - ANAHEIM WAY																																																							
103	5 - N/O KATELLA TO ORANGEWOOD	579 days	Tue 10/1/19	Sun 12/19/21	5 - N/O KATELLA TO ORANGEWOOD																																																							
104	Administration	3 emo	Tue 10/1/19	Mon 12/30/19	Administration																																																							
105	Final PS&E	9 emo	Mon 12/30/19	Fri 9/25/20	Final PS&E																																																							
106	Bid / Award / NTP	3 emo	Fri 9/25/20	Thu 12/24/20	Bid / Award / NTP																																																							
107	Construction	12 emo	Thu 12/24/20	Sun 12/19/21	Construction																																																							

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months

Administration		Right of Way Acquisition		Construction		Milestone	
Preliminary Engineering		Final PS&E		Task		Summary	
Right of Way Engineering		Bid / Award / NTP		Split		Progress	



CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS

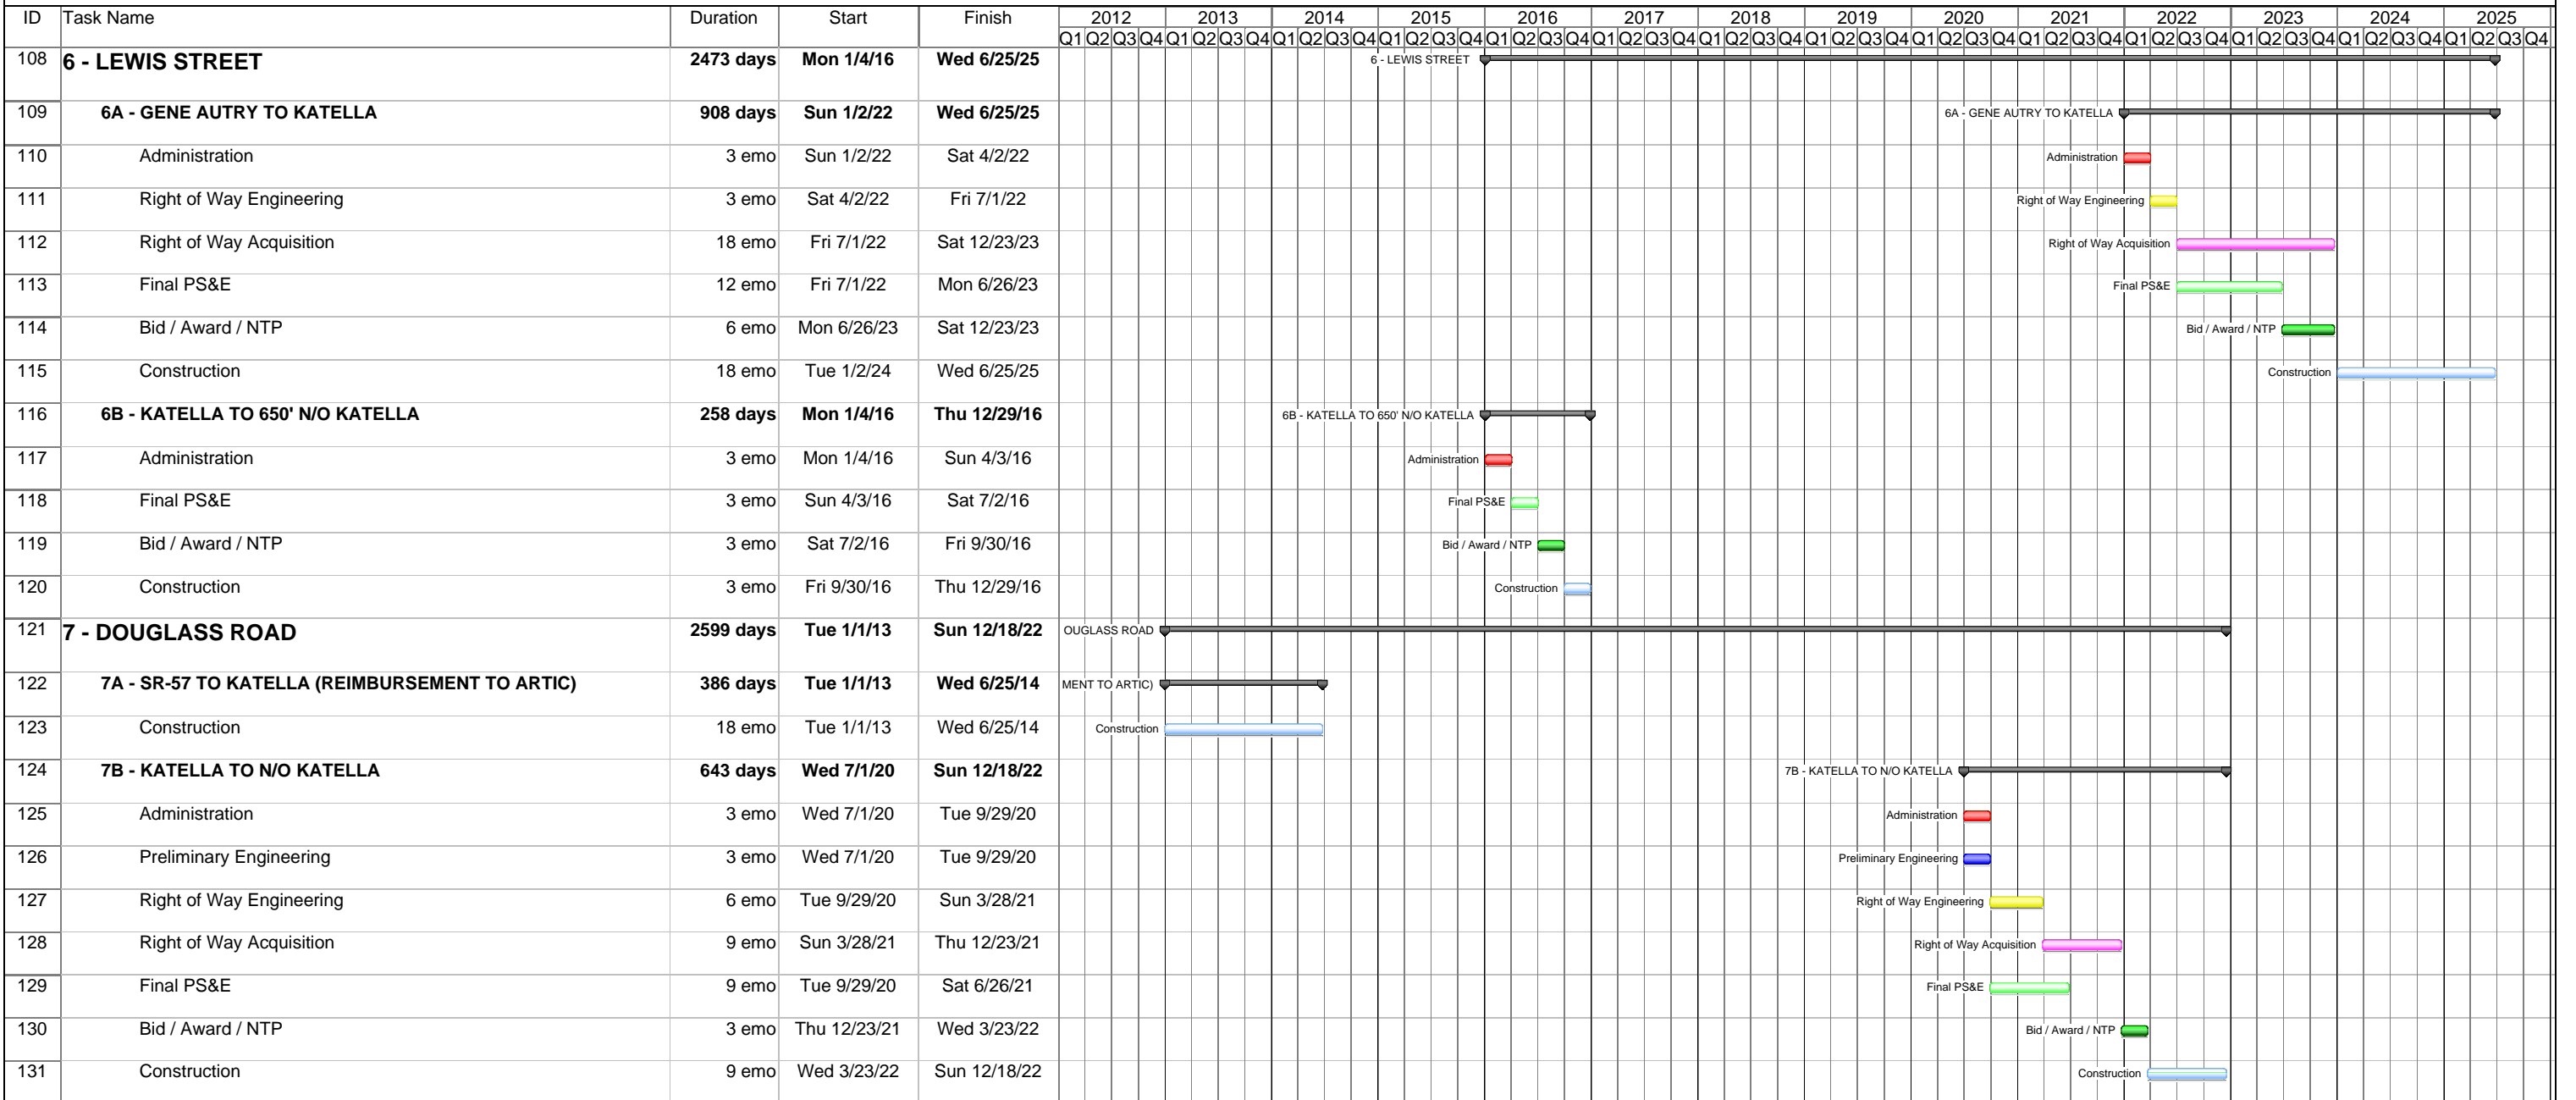

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months












Administration		Right of Way Acquisition		Construction		Milestone	
Preliminary Engineering		Final PS&E		Task		Summary	
Right of Way Engineering		Bid / Award / NTP		Split		Progress	



CITY OF ANAHEIM
PLATINUM TRIANGLE
IMPLEMENTATION PLAN FOR PUBLIC WORKS BACKBONE FACILITIES IMPROVEMENTS

ID	Task Name	Duration	Start	Finish	2012				2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025			
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4												
154	13 - CITY OF ORANGE INTERSECTIONS	792 days	Thu 9/30/21	Mon 10/14/24	13 - CITY OF ORANGE INTERSECTIONS																																																							
155	Administration	3 emo	Thu 9/30/21	Wed 12/29/21	Administration																																																							
156	Preliminary Engineering	3 emo	Wed 12/29/21	Tue 3/29/22	Preliminary Engineering																																																							
157	Right of Way Engineering	3 emo	Tue 3/29/22	Mon 6/27/22	Right of Way Engineering																																																							
158	Right of Way Acquisition	12 emo	Mon 6/27/22	Thu 6/22/23	Right of Way Acquisition																																																							
159	Final PS&E	12 emo	Mon 6/27/22	Thu 6/22/23	Final PS&E																																																							
160	Bid / Award / NTP	4 emo	Thu 6/22/23	Fri 10/20/23	Bid / Award / NTP																																																							
161	Construction	12 emo	Fri 10/20/23	Mon 10/14/24	Construction																																																							
162	14 - CERRITOS AVENUE	708 days	Wed 7/1/20	Sat 3/18/23	14 - CERRITOS AVENUE																																																							
163	14A - 550' W/O STATE COLLEGE TO 600' E/O STATE COLLEGE	708 days	Wed 7/1/20	Sat 3/18/23	14A - 550' W/O STATE COLLEGE TO 600' E/O STATE COLLEGE																																																							
164	Administration	3 emo	Wed 7/1/20	Tue 9/29/20	Administration																																																							
165	Preliminary Engineering	3 emo	Tue 9/29/20	Mon 12/28/20	Preliminary Engineering																																																							
166	Final PS&E	12 emo	Mon 12/28/20	Thu 12/23/21	Final PS&E																																																							
167	Right of Way Acquisition	12 emo	Mon 12/28/20	Thu 12/23/21	Right of Way Acquisition																																																							
168	Bid / Award / NTP	3 emo	Thu 12/23/21	Wed 3/23/22	Bid / Award / NTP																																																							
169	Construction	12 emo	Wed 3/23/22	Sat 3/18/23	Construction																																																							

Fiscal Year = July 1 - June 30
 emo = Elapsed (Calendar) Months

Administration 	Right of Way Acquisition 	Construction 	Milestone 
Preliminary Engineering 	Final PS&E 	Task 	Summary 
Right of Way Engineering 	Bid / Award / NTP 	Split 	Progress 
